


SEDIMENT & EROSION CONTROL PLAN

~ 1:100


Sediment and erosion control measures are to be installed prior to any excavation works are carried out on site.
Installations are to be continually reviewed, maintained, upgraded to ensure satisfactory control of sediment and erosion.

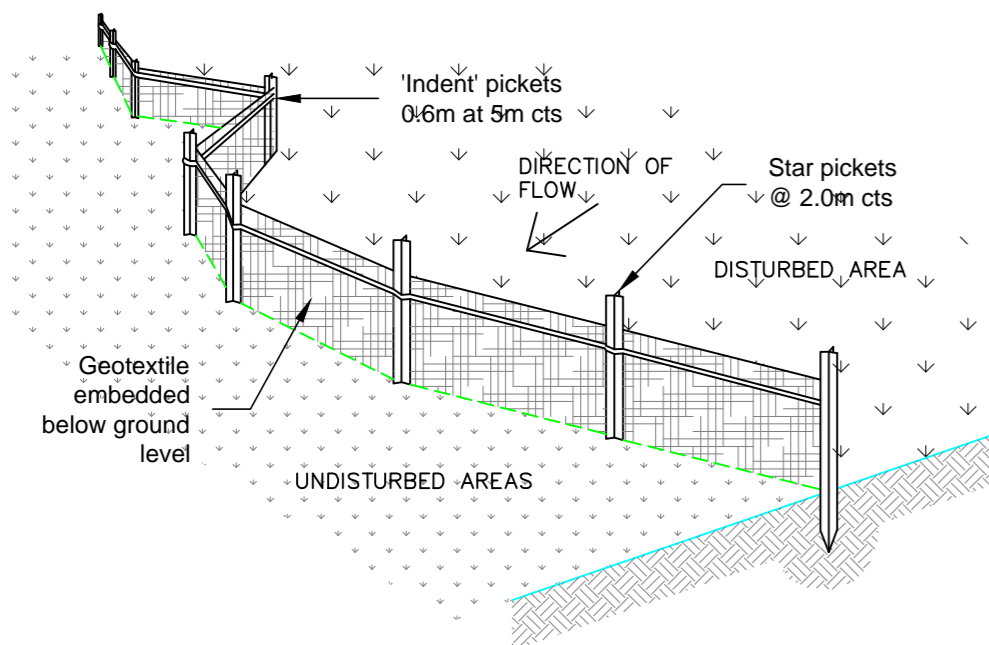

SEDIMENT FENCE

SEDIMENT FENCE CONSTRUCTION NOTES:

1. CONSTRUCT SEDIMENT FENCES AS CLOSE AS POSSIBLE TO BEING PARALLEL TO THE CONTOURS OF THE SITE, BUT WITH SMALL RETURNS AS SHOWN IN THE DRAWING TO LIMIT THE CATCHMENT AREA OF ANY ONE SECTION. THE CATCHMENT AREA SHOULD BE SMALL ENOUGH TO LIMIT WATER FLOW.
2. CUT A 150mm DEEP TRENCH ALONG THE UPSLOPE LINE OF THE FENCE FOR THE BOTTOM OF THE FABRIC TO BE ENTRENCHED.
3. DRIVE 1.5m LONG STAR PICKETS INTO GROUND @ 2.5m INTERVALS (MAX.) AT THE DOWNSLOPE EDGE OF THE TRENCH. ENSURE ANY STAR PICKETS ARE FITTED WITH SAFETY CAPS.
4. FIX SELF-SUPPORTING GEOTEXTILE TO THE UPSLOPE SIDE OF THE POSTS ENSURING IT GOES TO THE BASE OF THE TRENCH. FIX THE GEOTEXTILE WITH WIRE TIES OR AS RECOMMENDED BY THE MANUFACTURER. ONLY USE GEOTEXTILE SPECIFICALLY PRODUCED FOR SEDIMENT FENCING. THE USE OF SHADE CLOTH FOR THIS PURPOSE IS NOT SATISFACTORY.
5. JOIN SECTIONS OF FABRIC AT A SUPPORT POST WITH A 150mm OVERLAP.
6. BACKFILL THE TRENCH OVER THE BASE OF THE FABRIC AND COMPACT IT THOROUGHLY OVER THE GEOTEXTILE.

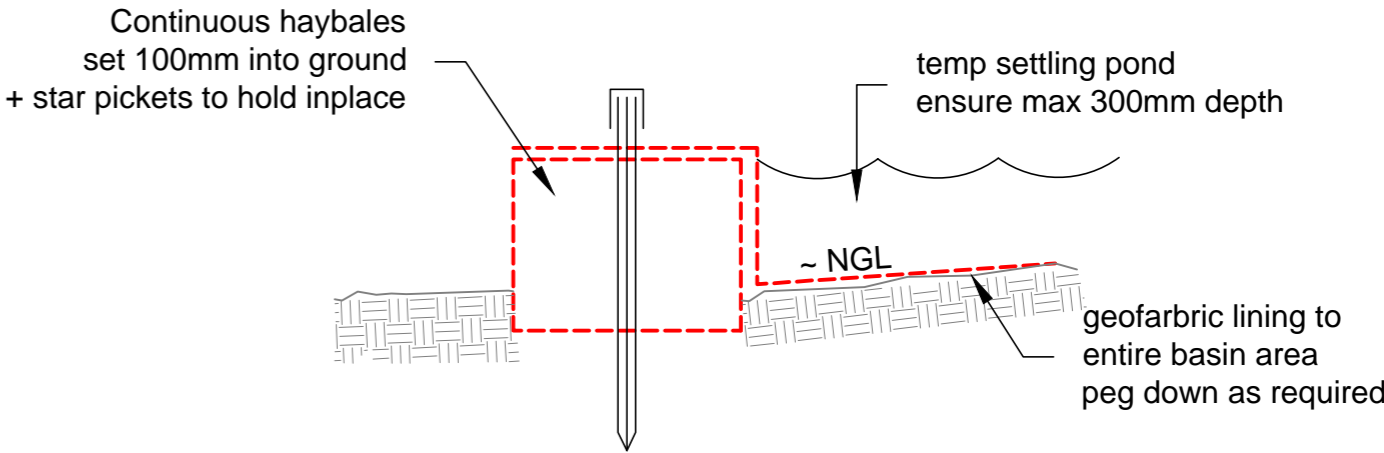

HAY BALE / SETTLING POND DETAIL

ISSUE:			Barrenjoey Consulting Engineers <small>pty ltd</small> <i>Stormwater Structural Civil</i> PO Box 672 Avalon NSW 2107 M: 0418 620 330 E: lucasbce@bigpond.com ABN: 13124694917 ACN: 124694917	PROJECT: PROPOSED NEW RESIDENCE 33 HILLCREST RD MONA VALE for ~ STEVENS FAMILY	DRAWING : SEDIMENT & EROSION CONTROL PLAN	Job No : 181103	Drawing No : CIV1 Prelim
06. 12. 2018	Prelim	issued for comment				Document Certification Barrenjoey Consulting Engineers <small>pty ltd</small> per Lucas Molloy <small>MIEA CPEng NER Director</small>	
