


SEDIMENT CONTROL NOTES

- All erosion and sedimentation control measures, including revegetation and storage of soil and topsoil, shall be implemented to the standards of the soil conservation of nsw.
- 2. All drainage works shall be constructed and stabilized as early as possible during development.
- Sediment traps shall be constructed around all inlet pits, consisting of 300 mm wide x 300 mm deep trench.
- All sediment basins and traps shall be cleaned when the structures are a maximum of 60 % full of soil materials, including the maintenance period.
- 5. All disturbed areas shall be revegitated as soon as the relevant works are completed.
- Soil and topsoil stockpiles shall be located away from drainage
- Innes and area where water may concentrate.
 Filter shall be constructed by stretching a filter fabric (propex or approved equivalent between post at 3.0m centres. Fabric shall be buried 150mm along its lower edge.




MS C WATMAN 29 PEACOCK PARADE FRENCHS FOREST NSW 2086

EROSION & SEDIMENTATION CONTROL PLAN



A.B.N. 54 000 605 407

SUITE 41, 410 CHURCH STREET, NORTH PARRAMATTA 2151 PHONE: (02) 9849 4444 BUILDERS LICENCE NO. 5519

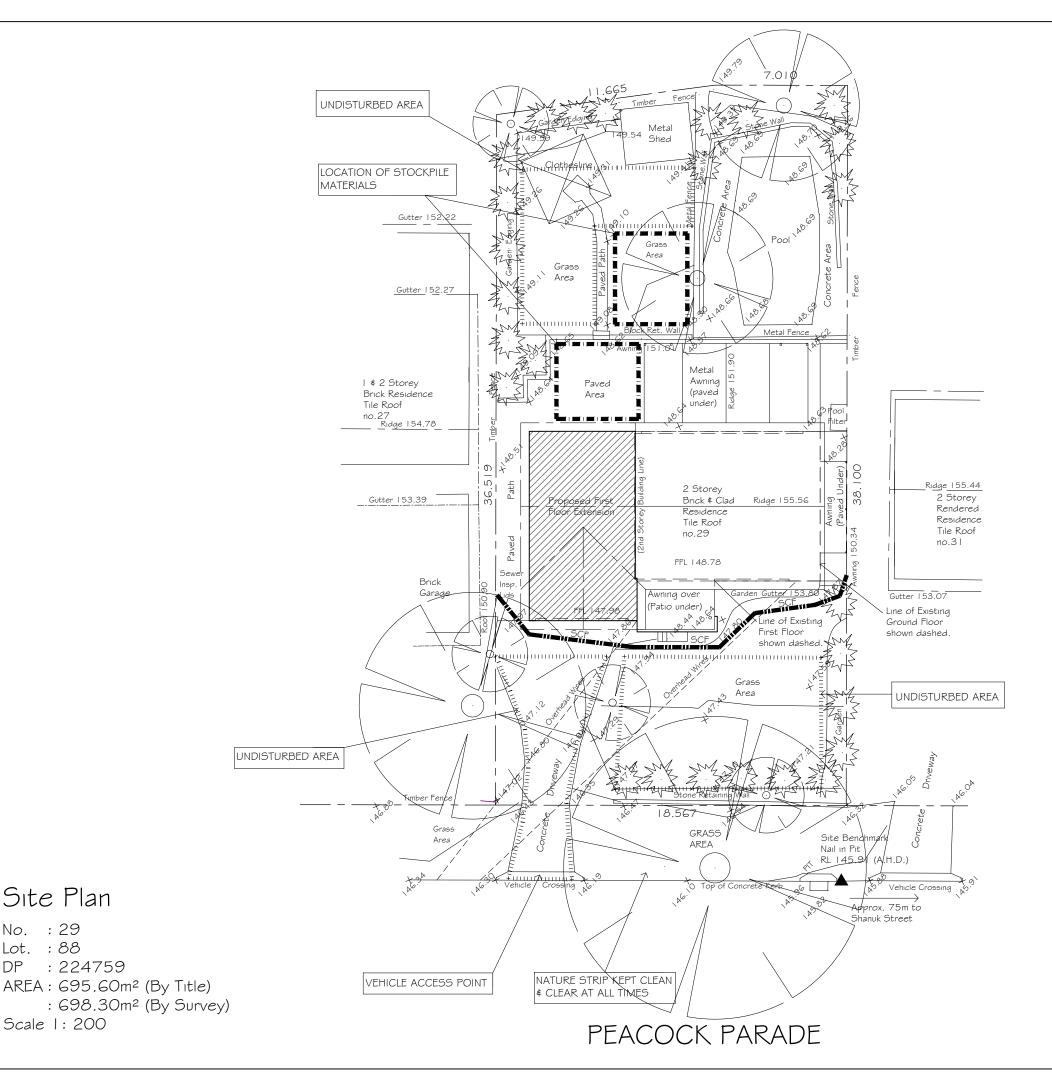

Site Plan

DP : 224759

Scale 1: 200

No. : 29

Lot. : 88
