LEGEND:							DE
MH	SEWER MAIN AND DIRECTION OF FLOW		POTABLE WATER MAIN	VC	VITRIFIED CLAY	DIMENSIONS REFLECTED IN THIS PLAN	PE
	SYDNEY WATER SEWER MAN-HOLE		- HYDRANT	S.O. PEG	SQUARE OFF	MAY NEED TO BE CONFIRMED BY EXCAVATION EXPOSING THE SYDNEY WATER ASSET	
— o —	MAINTENANCE SHAFT	—×—	STOP VALVE		PEG IN GOUND	PRIOR TO CONSTRUCTION COMMENCING ON SITE	
R ^P	RODDING POINT	DICL	DUCTILE IRON CEMENT LINED	NAIL	NAIL IN GROUND OR ON WALL		
VSL	VENTSHAFT (INDUCT OR EDUCT)	EW	EARTHENWARE	BDY	BOUNDARY		
OVER	VERTICAL RISER	RC	REINFORCED CONCRETE	EX.	EXISTING		
	P.C.P. OR JUNCTION	SGW	SALT GLAZED WARE	DN	DIAMETER		
		C/L	CENTRE LINE	0	PEG		

PLEASE REFER TO SYDNEY WATER HYDRA (TOP RIGHT CORNER) FOR DIAGRAM OF THE ASSETS ON SITE.

NO BOUNDARIES OR STRUCTURES IDENTIFIED ON SITE TO TIE IN SEWER, A REGISTERED SURVEYOR HAS PROVIDED AUSFLOW WITH THE MEASUREMENTS TO SYDNEY WATER ASSETS FROM REAR BOUNDARY CORNERS (AUSFLOW LOCATED SEWER ON SITE, WITH PEGS IN GROUND FOR REFERENCE POINT)

AUSFLOW HOLD NO WARRANTY FOR THE ACCURACY OF THE SURVEYORS MEASUREMENTS.


PIPE MATERIAL TO BE CONFIRMED PRIOR TO CONSTRUCTION, IF CONCRETE ENCASEMENT IS REQUIRED.

MANHOLE HAS BEEN UPGRADED ON SITE AND PIPE MATERIAL IS NOT VISIBLE, DUE TO PVC PIPE ACTING AS PIPE REHAB (PIPE FIXED) INSIDE MANHOLE.


NOTES:

- 1. CONTRACTOR TO LOCATE LINE, LEVEL AND SIZE OF ALL THE EXISTING SERVICES (AS PER NOTE ON PLAN) WITHIN THE VICINITY OF ANY NEW WORKS AND REPORT ANY CONFLICT TO SITE SUPERINTENDENT PRIOR TO ANY CONSTRUCTION COMMENCING
- Ausflow PTY LTD
 Ph: (02) 9555 7979
 Email: info@ausflowsydney.com.au
 Web: www.ausflowsydney.com.au
 ALLOCATED AS PEG-OUT / ASSET LOCATORS FOR SYDNEY WATER
- 3. THE LOCATION OF THE ASSETS SPECIFIED ON THIS PLAN ARE REFLECTED IN ACCORDANCE WITH SURVEYORS MARKINGS OR PEGS. MEASUREMENTS MAY HAVE ALSO BEEN TAKEN FROM EX. FENCES AND HYDRA
- 4. THIS PLAN IS NOT TO SCALE, DO NOT SCALE FROM THIS PLAN REFER DIMENSIONS SHOWN
- 5. SYDNEY WATER WORK AS EXECUTED (WAE) RECORDS AND HYDRA MAY HAVE BEEN USED TO <u>ASSIST</u> IN DETERMINING THE LOCATIONS AND DEPTHS OF THE ASSETS SPECIFIED IN THIS PLAN
- 6. MEASUREMENTS TAKEN FROM EXISTING FENCE LINES AND STRUCTURES ON SITE, FENCE LINES AND STUCTURES MAY NOT BE TRUE BOUNDARY MARKS ON SITE.

SEWER LOCATED VIA ELECTRONIC DETECTION ON SITE. PEGS AND PAINT USED TO MARK OUT SEWER ON SITE.

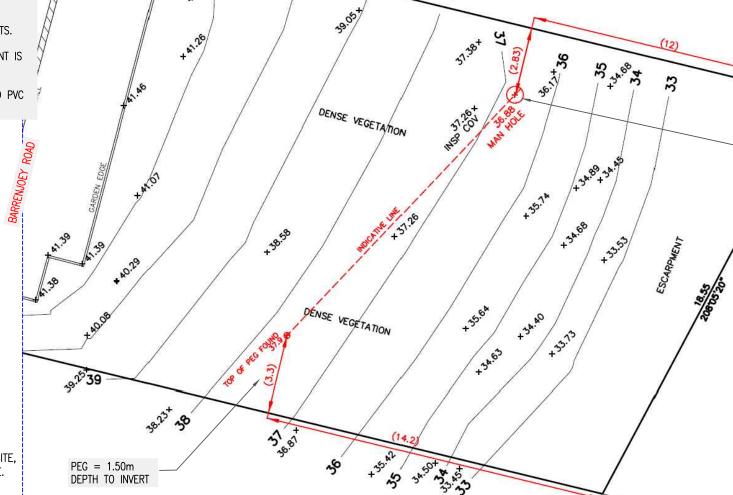

PLAN TO BE READ IN CONJUNCTION	UTILITIES LOCATED:				SITE STRATA (CIRCLE APPLICABLE)							PROPERTY ADDRESS:		
WITH CURRENT SURVEY PLAN	SERVICE	DATE	SIZE (mm)	TYPE	CLAY	DAAR	ROCK	SAND	SHALE	TUNNEL	RUBBISH		190	
	EXISTING SEWER:	29/11/17	150	ABS			TRENCH						Barrenjoey Road	
	EXISTING SEWER:												Newport	
	STORMWATER: SWD SWD				I Gabriel Austin, of Ausflow Pty Ltd, being accredited to carry out a Service Protection Report / Peg-Out									
	COUNCIL STORM WATER PIPE				for Sydr	for Sydney Water, certify that the information shown on this plan has been prepared in accordance with								
	POTABLE WATER:				the relev	ant instruc	tions and st	andards						
GAS AGILITY Ph. 132 909 TELECOMM. TELSTRA Ph. 9204 0880		-		-										
TELECOWING TELSING Pri. 9204, 0880		-	-	-	1	LOCATOR SIGNATURE: JAW Har Date: 29/ 11 / 2017								
GIVE AT LEAST 48 HOURS NOTICE		_	-	-		LOC	CATOR SIG	NATURE: .	- Yu		Tra	Date: 29/ 11 / 2017	SHEET 1 OF 1 RE	

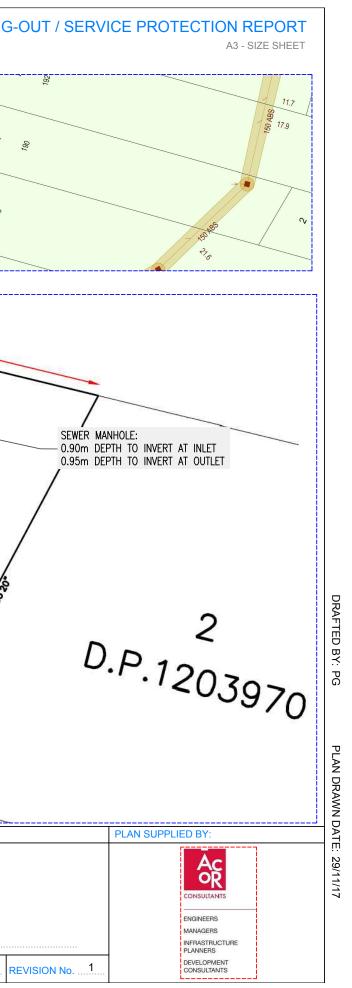

88
