

~ 1:200

All excavation works to be carried out in a safe building manner in accordance with BCA and industry standards etc. Sediment and erosion control measures to be installed before any excavation works and monitored / improved continually to prevent sediment leaving the site, including immediate cleaning of spillage etc from vehicles leaving the property. All material stock piles to be protected from rainfall and runoff at all times.

Barrenjoey Consulting Engineers Pty Itd Stormwater Structural Civil PO Box 672 Avalon NSW 2107 M: 0418 620 330 E: lucasbce@bigpond.com ABN: 13124694917 ACN: 124694917

PROJECT:

PROPOSED ALTERATIONS & ADDITIONS 3 BEACONSFIELD ST **NEWPORT** for ~ T. RUSHBY

DRAWING:

SEDIMENT & EROSION CONTROL PLAN


Job No:

Drawing No:

Document Certification

Lucas Molloy MIEA CPEng NER Director

Barrenjoey Consulting Engineers pty ltd

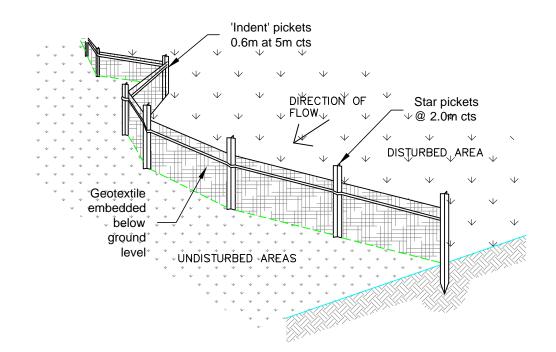

SEDIMENT FENCE

SEDIMENT FENCE CONSTRUCTION NOTES:

- CONSTRUCT SEDIMENT FENCES AS CLOSE AS POSSIBLE TO BEING PARALLEL TO THE CONTOURS OF THE SITE, BUT WITH SMALL RETURNS AS SHOWN IN THE DRAWING TO LIMIT THE CATCHMENT AREA OF ANY ONE SECTION. THE CATCHMENT AREA SHOULD BE SMALL ENOUGH TO LIMIT WATER FLOW.
- CUT A 150mm DEEP TRENCH ALONG THE UPSLOPE LINE OF THE FENCE FOR THE BOTTOM OF THE FABRIC TO BE ENTRENCHED.
- DRIVE 1.5m LONG STAR PICKETS INTO GROUND @ 2.5m INTERVALS (MAX.) AT THE DOWNSLOPE EDGE OF THE TRENCH. ENSURE ANY STAR PICKETS ARE FITTED WITH SAFETY CAPS.
- FIX SELF-SUPPORTING GEOTEXTILE TO THE UPSLOPE SIDE OF THE POSTS ENSURING IT GOES TO THE BASE OF THE TRENCH. FIX THE GEOTEXTILE WITH WIRE TIES OR AS RECOMMENDED BY THE MANUFACTURER. ONLY USE GEOTEXTILE SPECIFICALLY PRODUCED FOR SEDIMENT FENCING. THE USE OF SHADE CLOTH FOR THIS PURPOSE IS NOT SATISFACTORY.
- JOIN SECTIONS OF FABRIC AT A SUPPORT POST WITH A 150mm OVERLAP.
 BACKFILL THE TRENCH OVER THE BASE OF THE FABRIC AND COMPACT IT THOROUGHLY OVER THE GEOTEXTILE.

Barrenjoey Consulting Engineers ptyltd Stormwater Structural Civil

POBox 672 Avalon NSW 2107 M: 0418 620 330

E: lucasbce@bigpond.com ABN: 13124694917 ACN: 124694917

PROJECT:

PROPOSED ALTERATIONS & ADDITIONS 3 BEACONSFIELD ST **NEWPORT** for ~ T. RUSHBY

DRAWING:

SEDIMENT & EROSION CONTROL DETAILING

Job No:

Drawing No:

Document Certification

Barrenjoey Consulting Engineers pty ltd

Lucas Molloy MIEA CPEng NER Director
